


March 2018 MCCCH Construction Small Business Dashboard

Summary


- These charts are based on contracts and dollars awarded to date.
- The contractor's goal is to award 20% of total contract dollars to MWSDVESB firms. Currently, the MWSDVESB Contracted is 23.8% *

MCCCH MWSDVESB Firms Ethnicity




MCCCH Total Contracts Awarded

Total Contracts - 140



Multnomah County Central Courthouse Construction MWSDVESB Participation Hoffman Construction Contracted and Paid to Date

Goal: \$37.9 million (20% Participation) based on \$189* million total contracted to date. Hoffman Construction MWSDVESB Project to date 23.8%

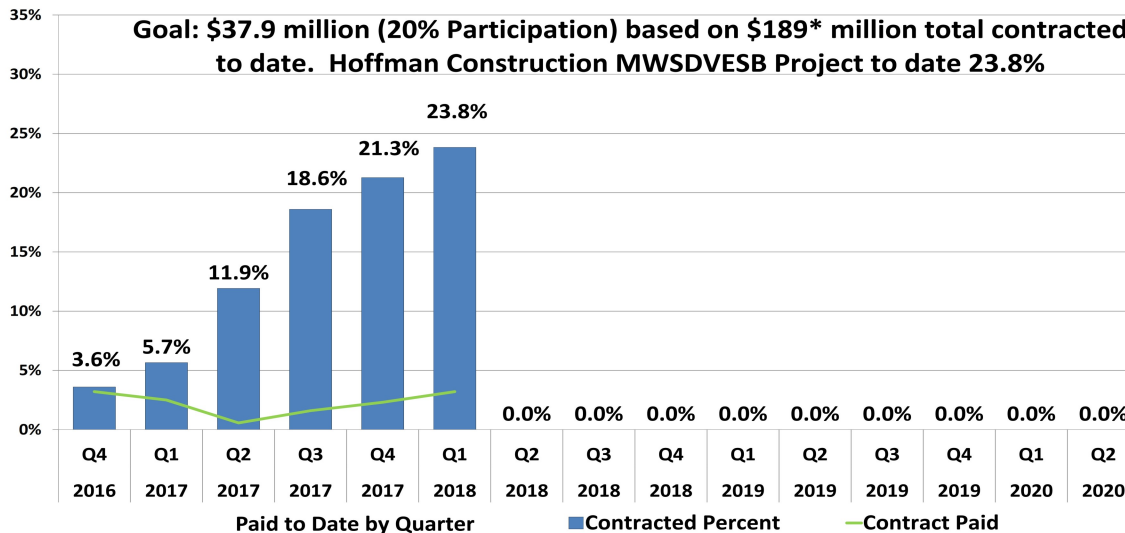

MCCCH MWSDVESB Participation By Dollars


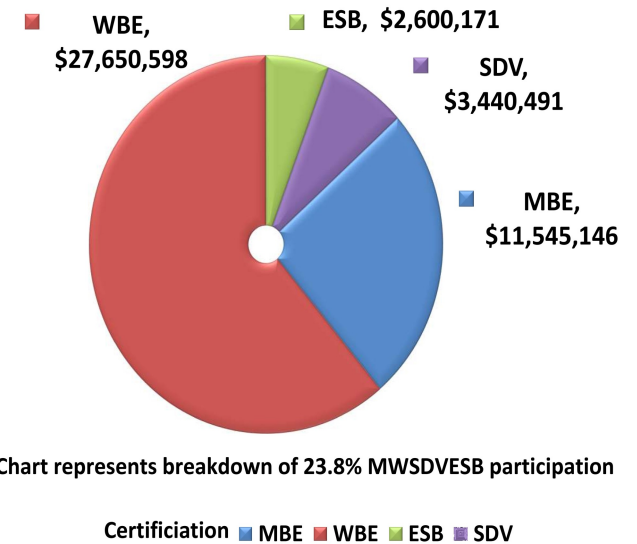


Chart represents breakdown of 23.8% MWSDVESB participation

Glossary: MBE—Minority-Owned Business, WBE—Women-Owned Business, ESB—Emerging Small Business, SDV - Service Disabled Veteran

*Represents adjusted GMP construction value
Cumulative Construction Data from 10/31/2016 to 3/30/2018.




March 2018 MCCCH Construction Workforce Dashboard


Project Summary

- Total Project Apprenticeship to date is 27%
- Project Goal is 20% apprenticeship by trade
- Project Total minority participation is 17% and female is 7.8%

Total Workforce Hours (Journey Level) 87,491 Hrs

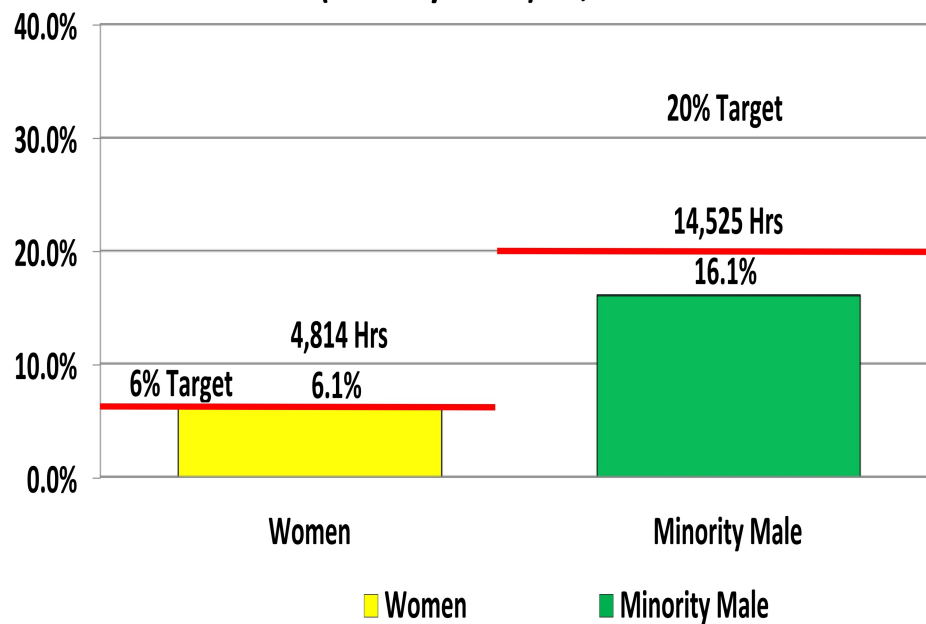


Total Workforce Hours (Apprentice Level) 30,092 Hrs

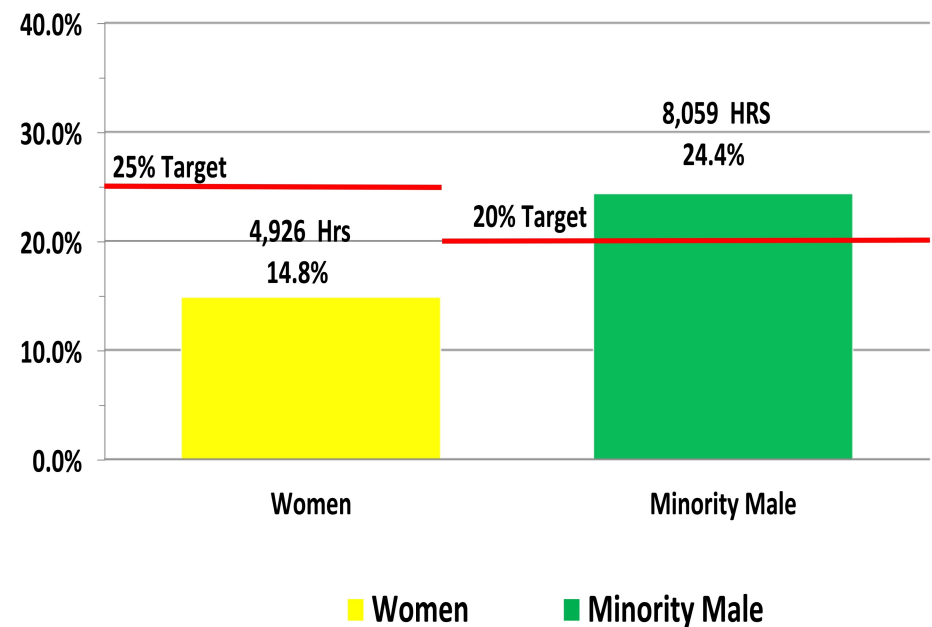


Cumulative Construction Data from 10/31/2016 to 3/30/2018

WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.




March 2018 MCCCH Construction Workforce Dashboard

MCCCH Apprenticeship by Trade

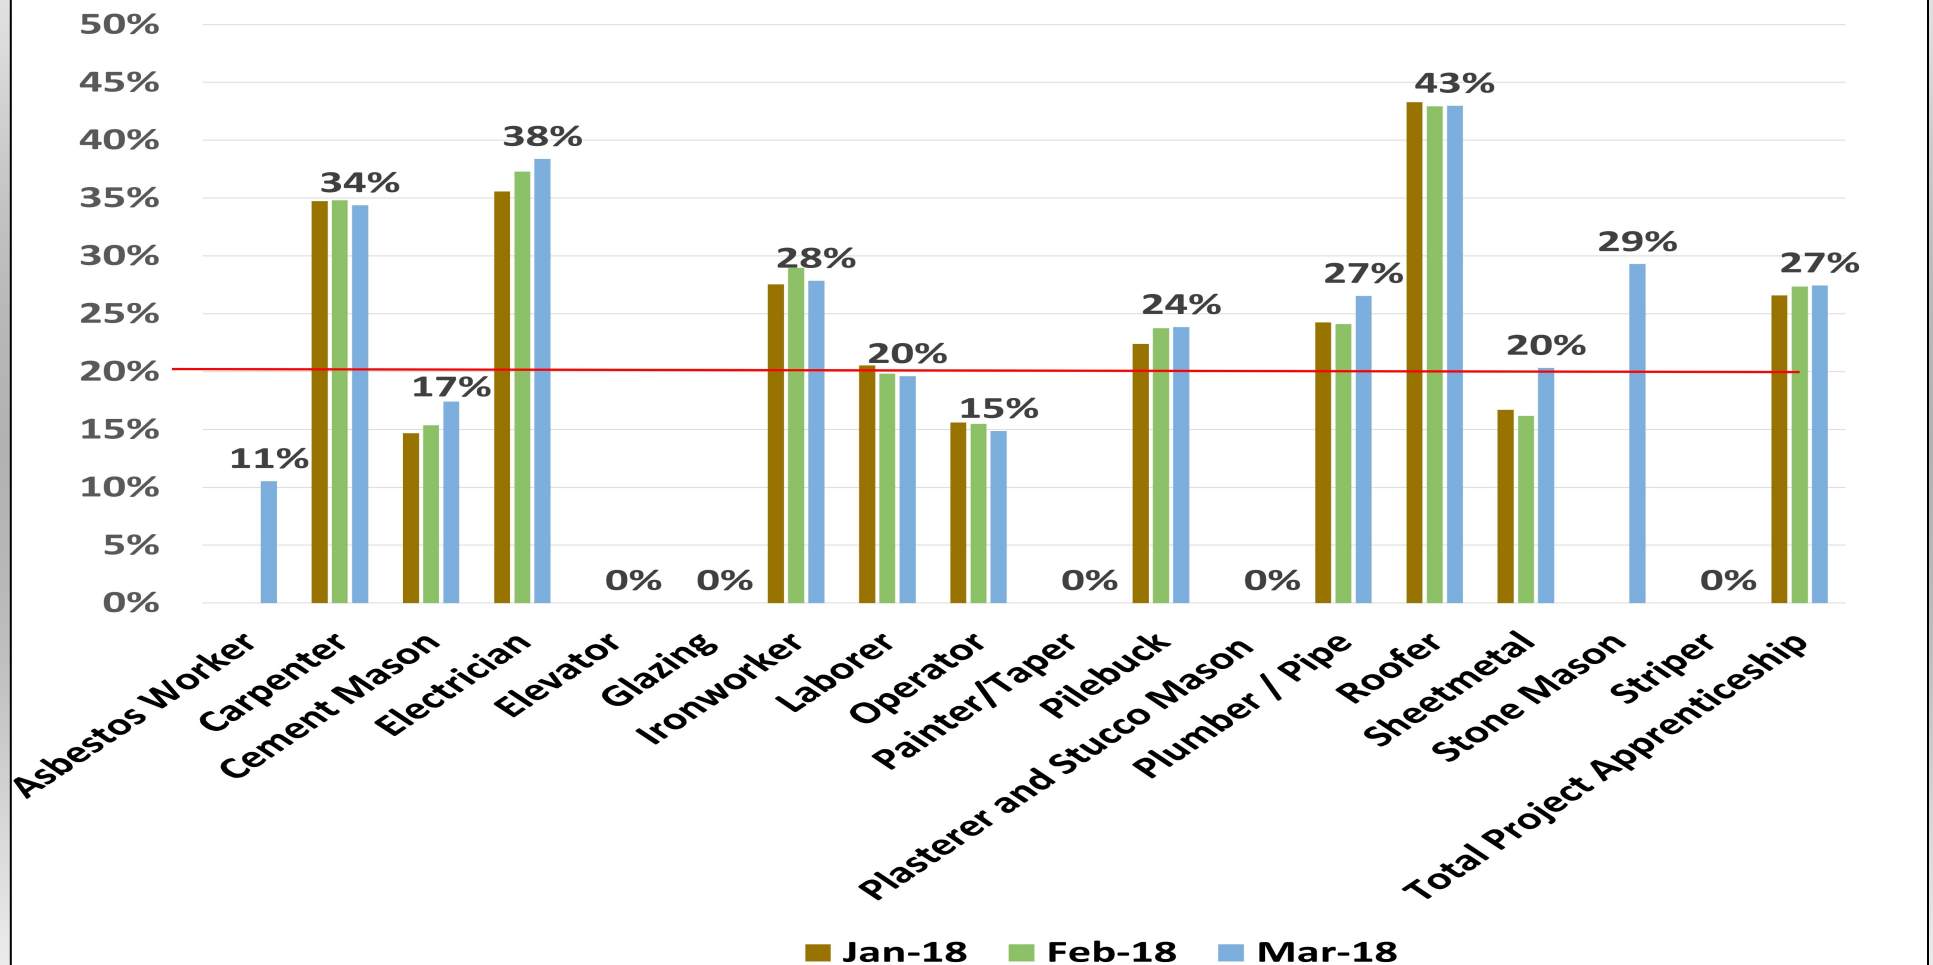

Cumulative Construction Data from 10/31/2016 to 3/30/2018

WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.




March 2018 MCCCH Construction Workforce Dashboard


Project Summary—


- Project has exceeded the 20% MWSDVESB Goal
- Continued communication with subs who have workforce / diversity shortfalls
- Working with subs to get their workforce / apprentice programs in place prior to mobilization
- Prefab stairs and slab edge curtainwall connections progressing
- PT structure up to Level 9

Total Male Workforce By Ethnicity

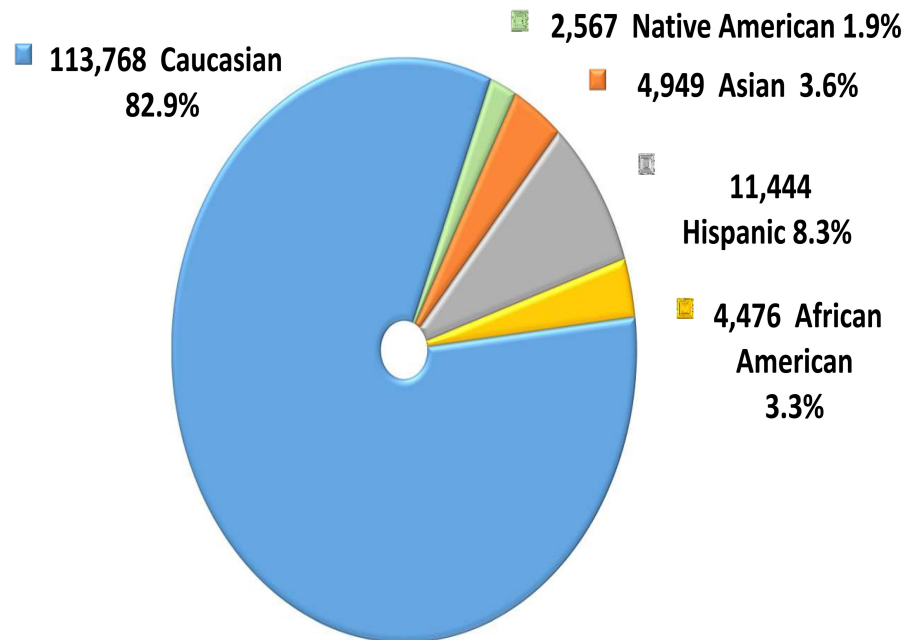

Total Female Workforce Ethnicity

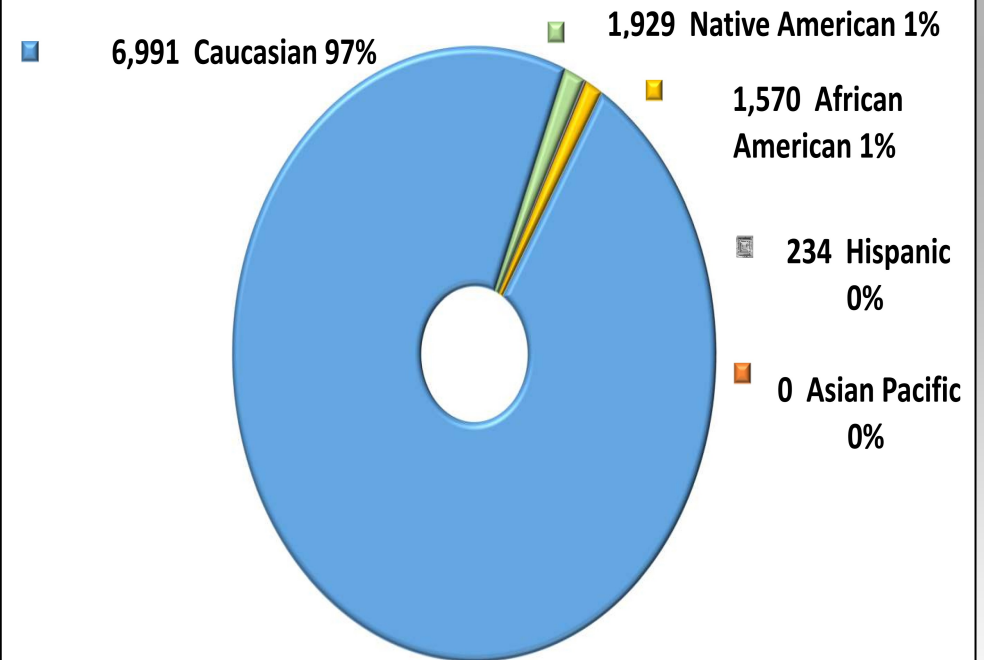




March 2018 MCCCH Construction

MWSDVESB Actual vs Forecast Percentage

MCCCH MWSDVESB Current Percentage 23.8% - March 2018

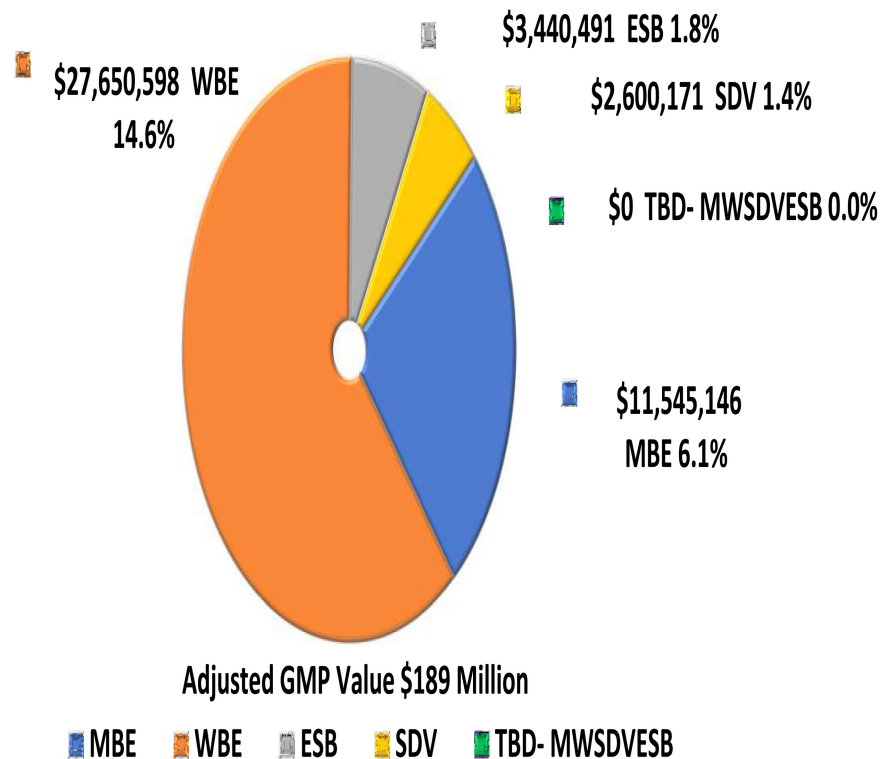

MCCCH MWSDVESB Forecast Percentage 26.3% - Dec 2020

