
July 2019 MCCCH Construction Small Business Dashboard



Glossary: MBE—Minority-Owned Business, WBE—Women-Owned Business, ESB—Emerging Small Business, SDV - Service Disabled Veteran


*Represents adjusted GMP construction value Cumulative Construction Data from 10/31/2016 to /31/2019

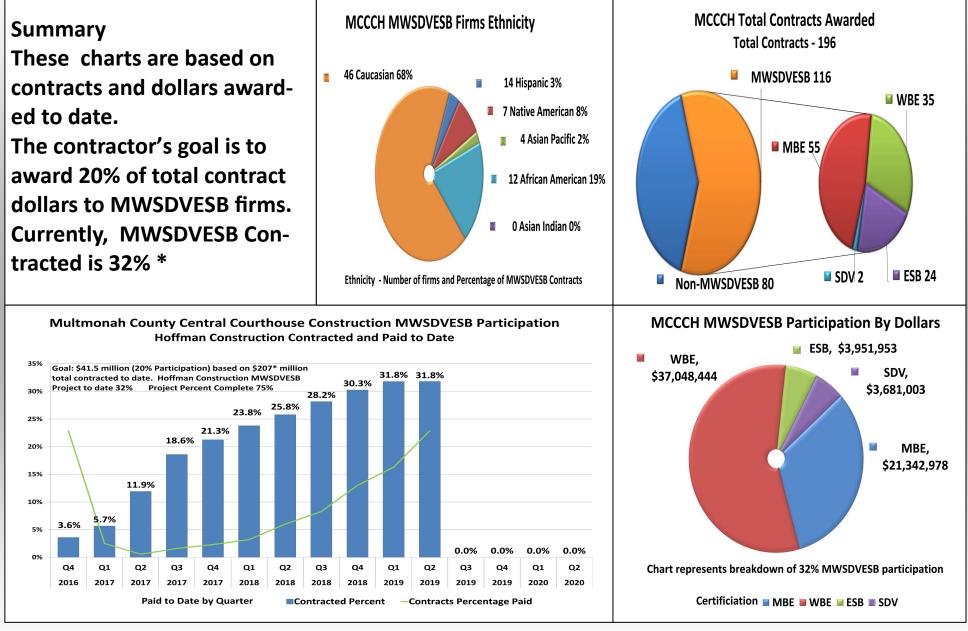

July 2019 MCCCH Construction Workforce Dashboard

Project Summary

- Total Project Apprenticeship to date is 30%
- Project Goal is 20% apprenticeship by trade
- Project Total minority male participation is 26% and female is 10.2%
- Project Percent Complete 80%

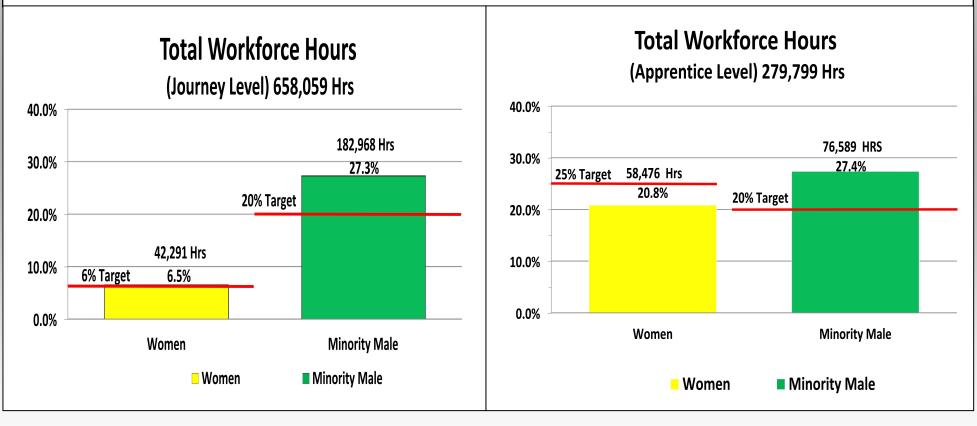


Cumulative Construction Data from 10/31/2016 to 7/31/2019

WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.



Construction Workforce Dashboard

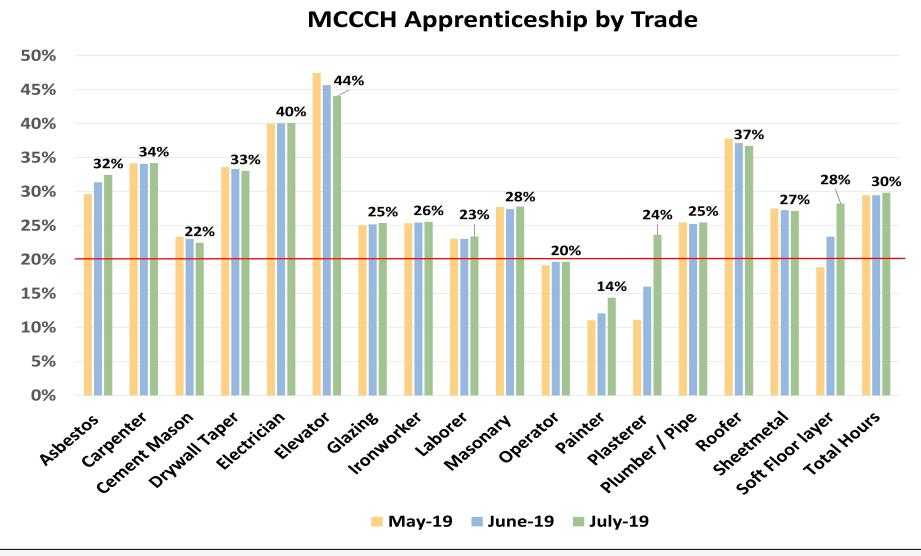


Cumulative Construction Data from 10/31/2016 to 7/31/2019 WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.



Construction Workforce Dashboard

MCCCH Minority Male Journey & Apprenticeship by Trade Hours

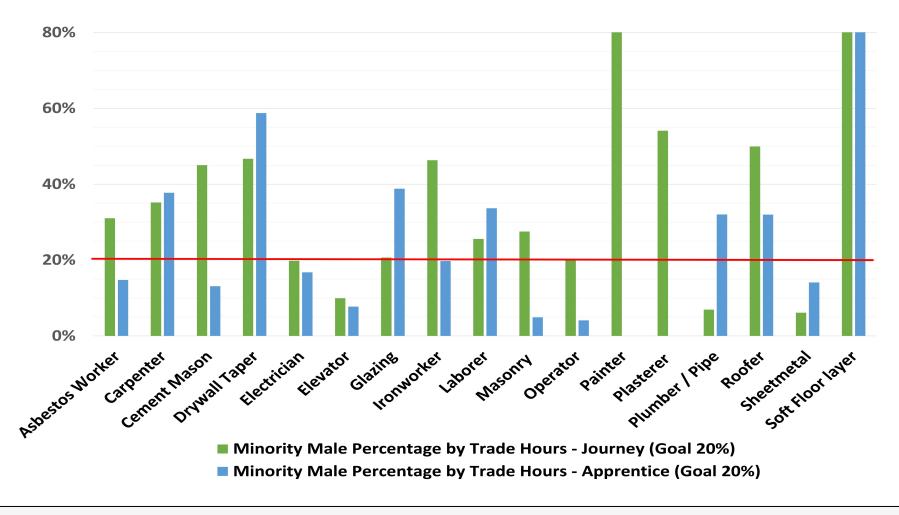


Cumulative Construction Data from 10/31/2016 to 7/31/2019 WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.



Construction Workforce Dashboard

MCCCH Female Journey & Apprenticeship by Trade Hours

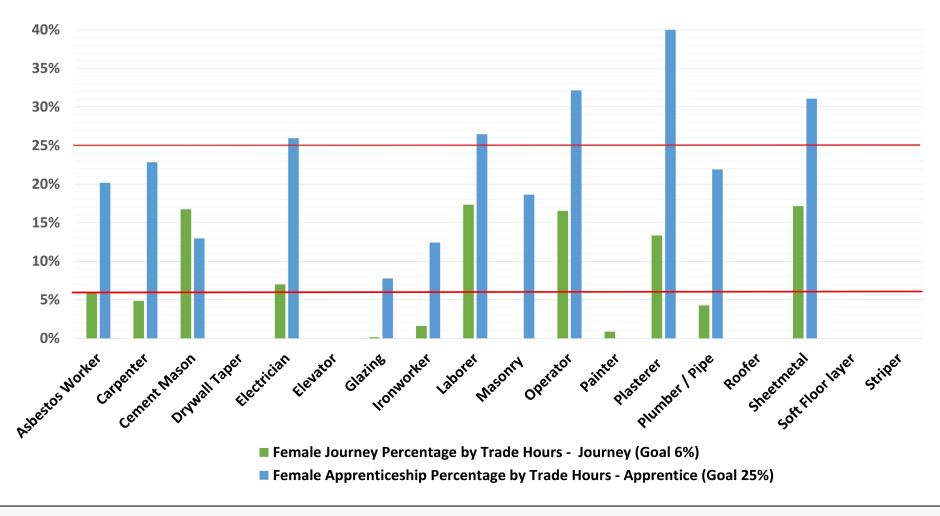


Cumulative Construction Data from 10/31/2016 to 7/31/2019 WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.



Construction Workforce Dashboard

Project Summary–

- Exceeding MWSDVESB and Overall Apprenticeship Goal
- . . 380+ Workers Daily Diversity is Consistent
- Landscape, Sitework and Final Cleaning Buyouts Complete
 - Added 2 MBE Firms
- Project Percent Complete 80%





July 2019 MCCCH Construction MWSDVESB Actual vs Forecast Percentage Project Percent Complete 80%

