

Project Update

Arata Road Active Transportation

Wood Village and Fairview



Transportation Division

Updated September, 2018

Project Scope

The project will build a complete streetscape on Arata Rd between NE 223rd Ave and NE 238th Dr., which includes:



Two traffic lanes



A 6-foot wide sidewalk on the south side



A 10-foot wide shared-use path for pedestrians and bicyclists on the north side



A 5-foot wide planting strip to treat stormwater between the north path and traffic lane

Project Schedule



Design completed and contractor, Wildish Standard Paving, selected.



February, 2017: Trees removed from work zone.



March - May, 2017: Utility poles relocated, heavy construction began.



February 2018: Natural gas lines relocated.



March - April, 2018: Utility poles relocated, heavy construction resumed.



Winter 2018/19: Project to shut down due to weather; two-lane traffic flow re-established.



Spring 2019: Project resumes, one-way traffic re-established.



Summer 2019: Road work ends.



Fall 2019: Planting ends. Project complete

Construction Impacts

- *During construction only*, Arata Rd traffic pattern changes from two-way traffic to one-way, flowing east from Wood Village Blvd to 238th Dr; and closing entirely between 223rd Ave and Wood Village Blvd.
- Contractor will build road in two phases (north and south sides).
- Pedestrian access maintained.
- Brief access interruptions during work at driveways, with prior notice.
- Coordination to ensure continued emergency vehicle access, mail delivery, garbage collection and school bus service.

Public Outreach & Planning




The project stems from the Arata Road Conceptual Design Plan developed in 2008 in partnership with the City of Wood Village. Arata Road has long been identified as a substandard street with safety concerns for pedestrians and cyclists, as well as drainage issues. Between 2008 and 2016 the County held open houses and outreach events to collect input on the design from community members, including local residents, members of churches in the area, and visitors to nearby shopping destinations.


February 26, 2018: A pre-construction public meeting was held at Wood Village Baptist Church.

September 24, 2018: A project update meeting for the public held at Wood Village Baptist Church.

The project is on Arata Rd. between NE 223rd and NE 238th Dr.

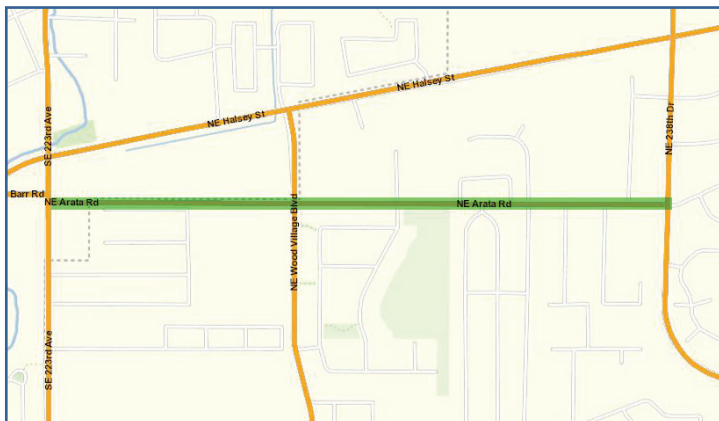

Sections of Arata Rd. on a school bus route currently lack sidewalks.

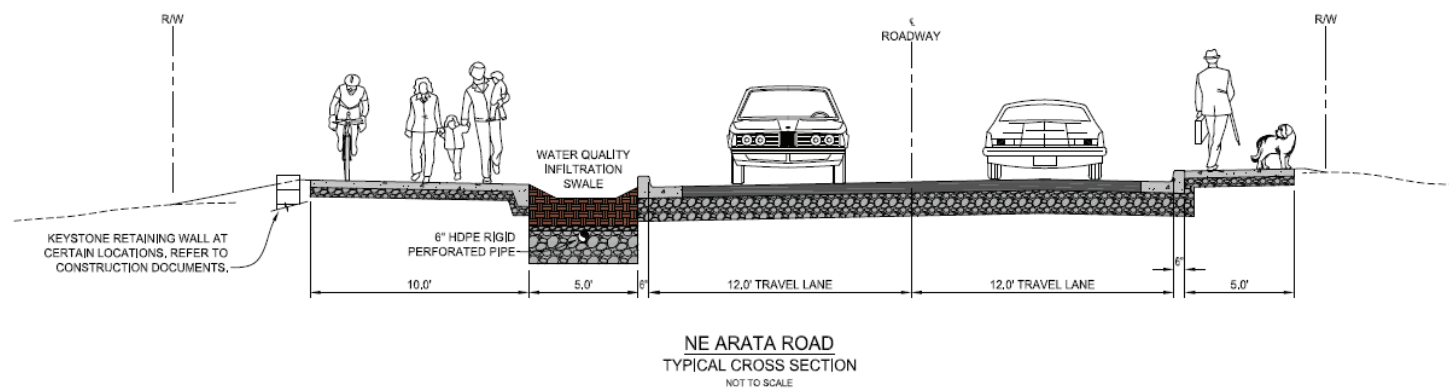

Budget Funding

The estimated construction cost is **\$4.5 million**. Funding comes from two federal sources with County General Roadway Funds.

For More Information



project website: www.multco.us/arata



Mike Pullen
Multnomah County Communications Office
503-209-4111
mike.j.pullen@multco.us
