

March 2019 MCCCH


Construction Small Business Dashboard

Summary

These charts are based on contracts and dollars awarded to date.


The contractor's goal is to award 20% of total contract dollars to MWSDVESB firms. Currently, MWSDVESB Contracted is 31.8% *

MCCCH MWSDVESB Firms Ethnicity




MCCCH Total Contracts Awarded


Total Contracts - 185

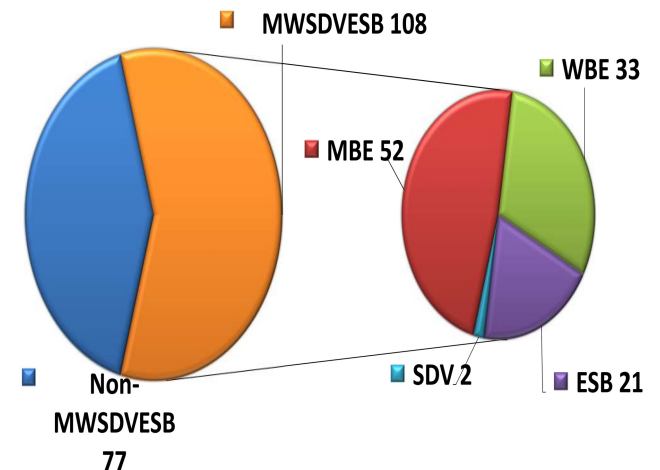

Multnomah County Central Courthouse Construction MWSDVESB Participation Hoffman Construction Contracted and Paid to Date

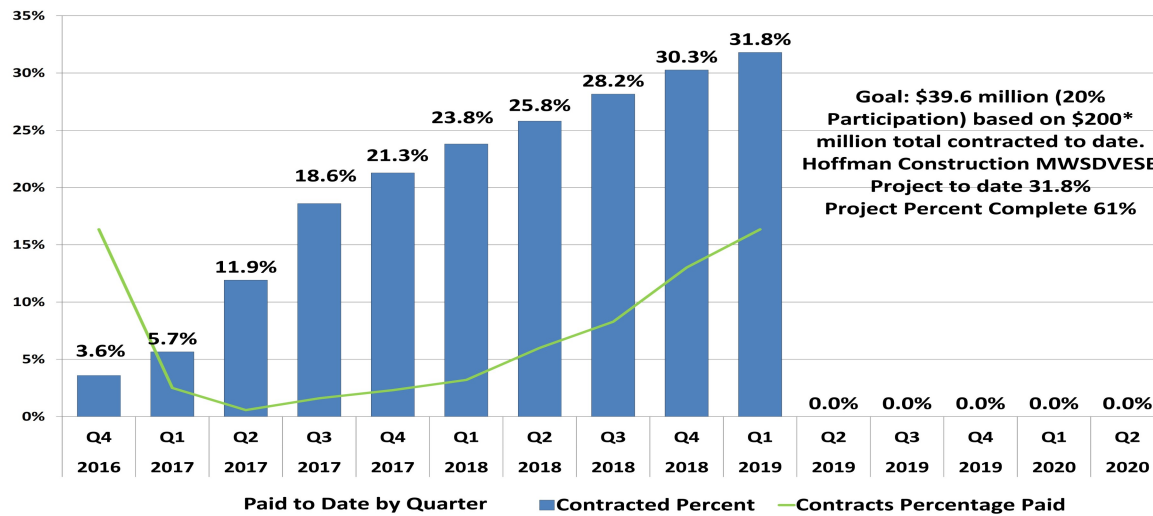


MCCCH MWSDVESB Participation By Dollars

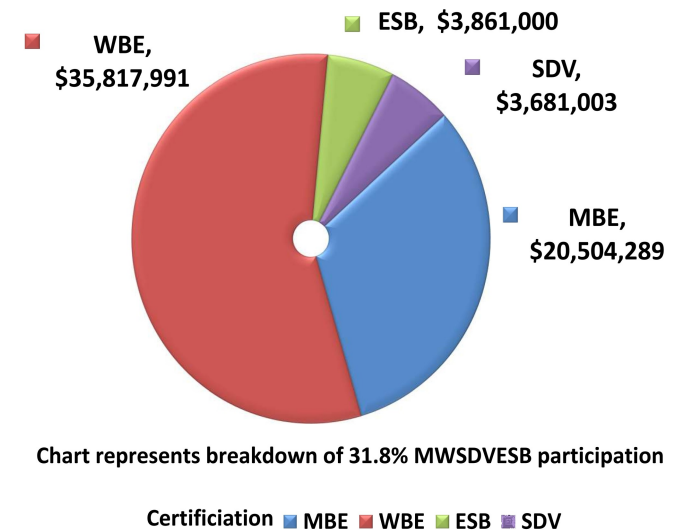

Glossary: MBE—Minority-Owned Business, WBE—Women-Owned Business, ESB—Emerging Small Business, SDV - Service Disabled Veteran

*Represents adjusted GMP construction value
Cumulative Construction Data from 10/31/2016 to 3/31/2019.




March 2019 MCCCH Construction Workforce Dashboard


Project Summary

- Total Project Apprenticeship to date is 29%
- Project Goal is 20% apprenticeship by trade
- Project Total minority participation is 25% and female is 10%
- Project Percent Complete 61%

Total Workforce Hours (Journey Level) 472,701 Hrs

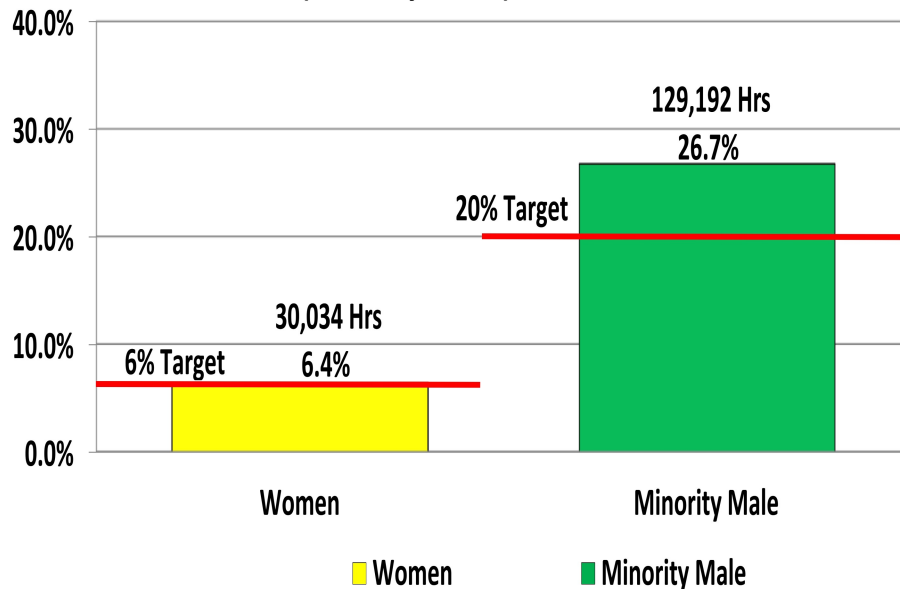

Total Workforce Hours (Apprentice Level) 194,389 Hrs

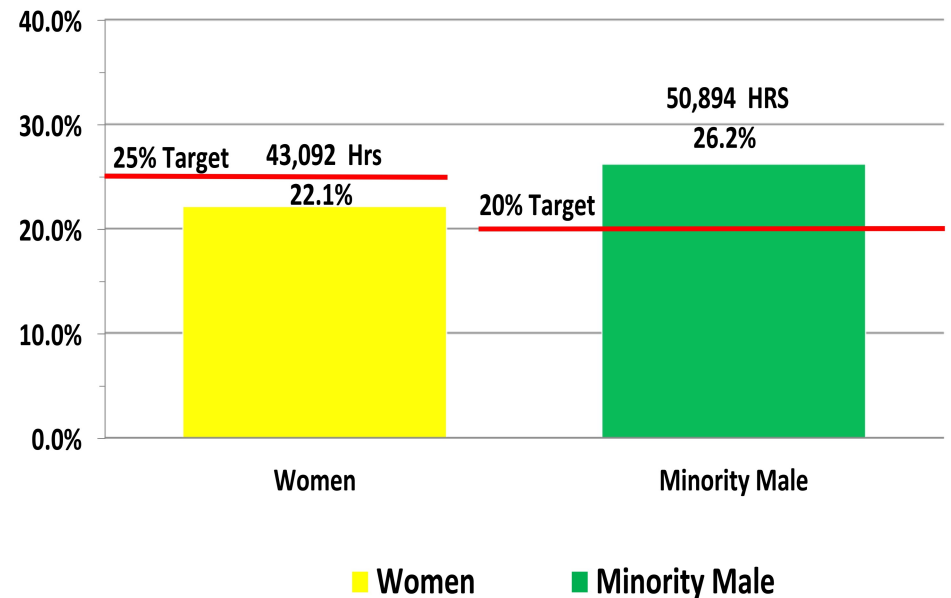

Cumulative Construction Data from 10/31/2016 to 3/31/2019


WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.



March 2019 MCCCH


Construction Workforce Dashboard

MCCCH Apprenticeship by Trade

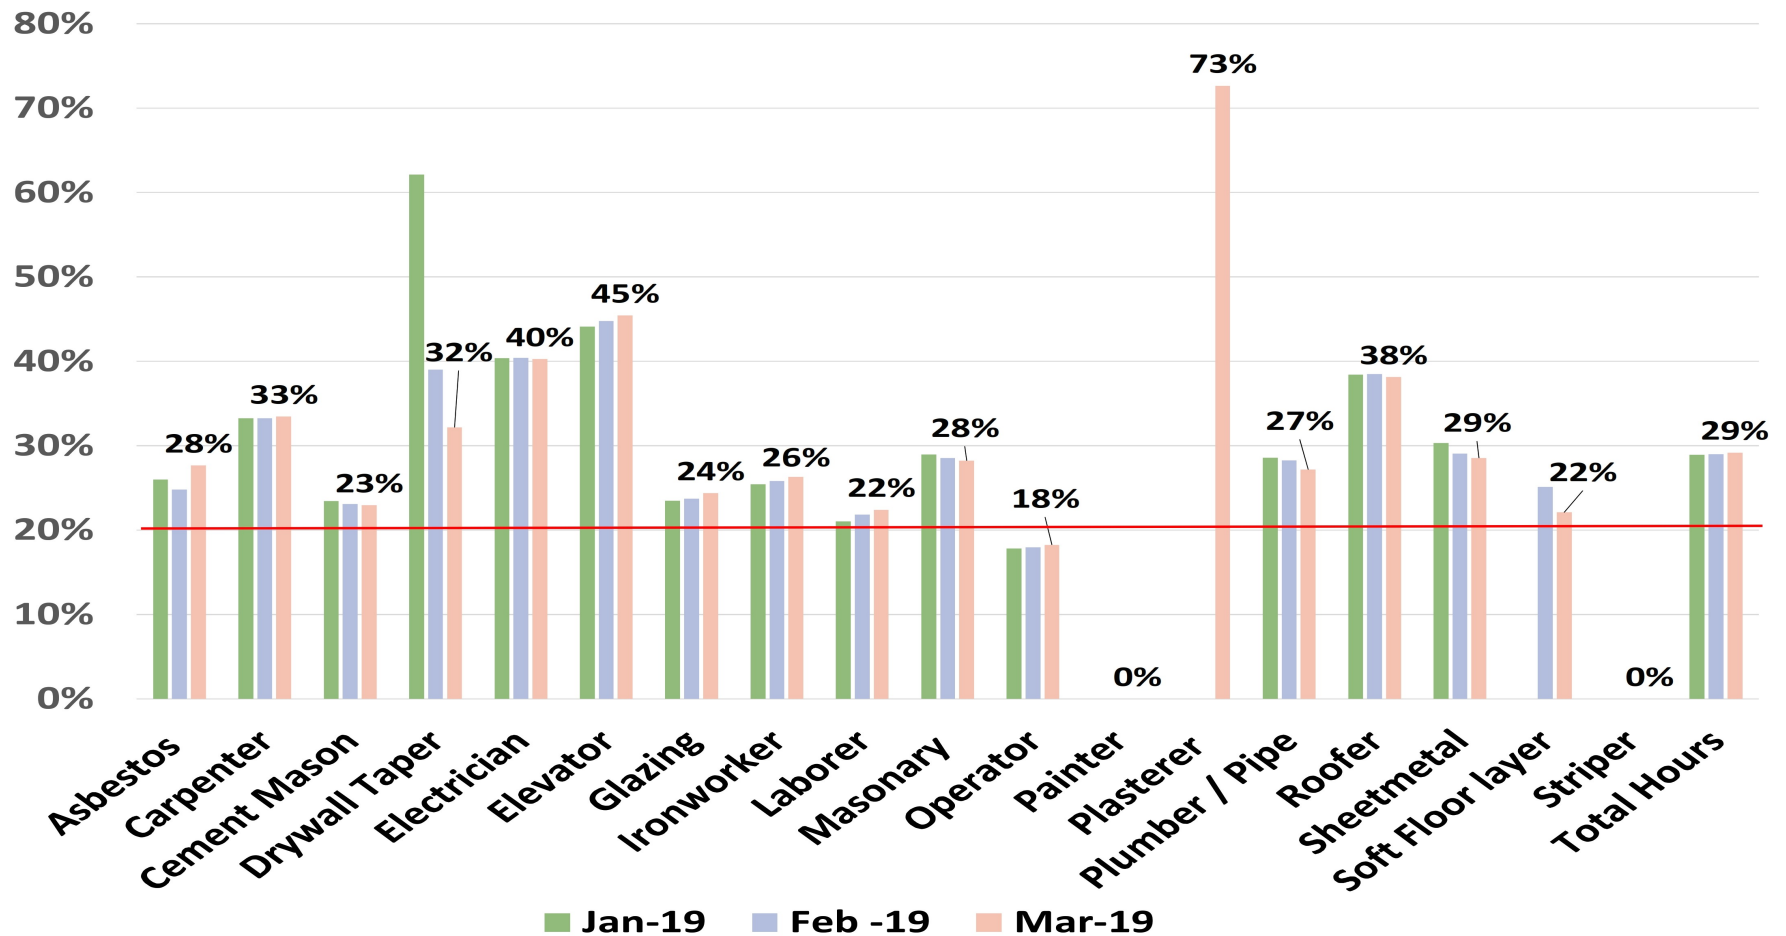

Cumulative Construction Data from 10/31/2016 to 3/31/2019


WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.



March 2019 MCCCH

Construction Workforce Dashboard

MCCCH Minority Male Journey & Apprenticeship by Trade Hours

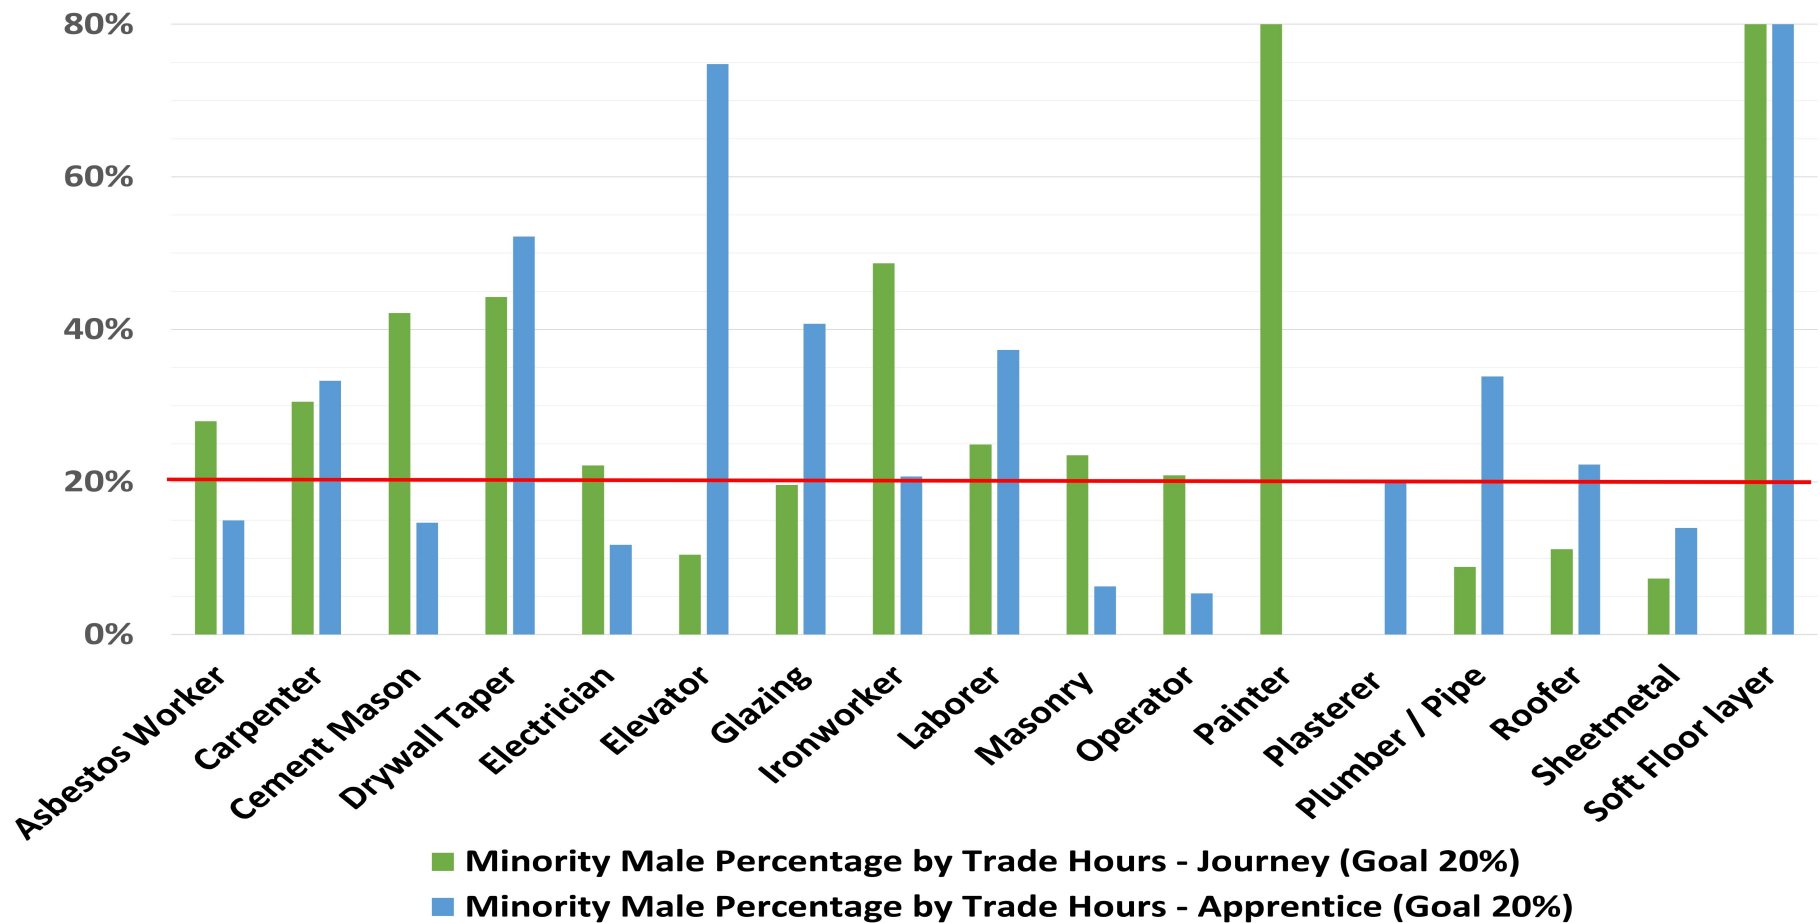

Cumulative Construction Data from 10/31/2016 to 3/31/2019


WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.



March 2019 MCCCH


Construction Workforce Dashboard

MCCCH Female Journey & Apprenticeship by Trade Hours

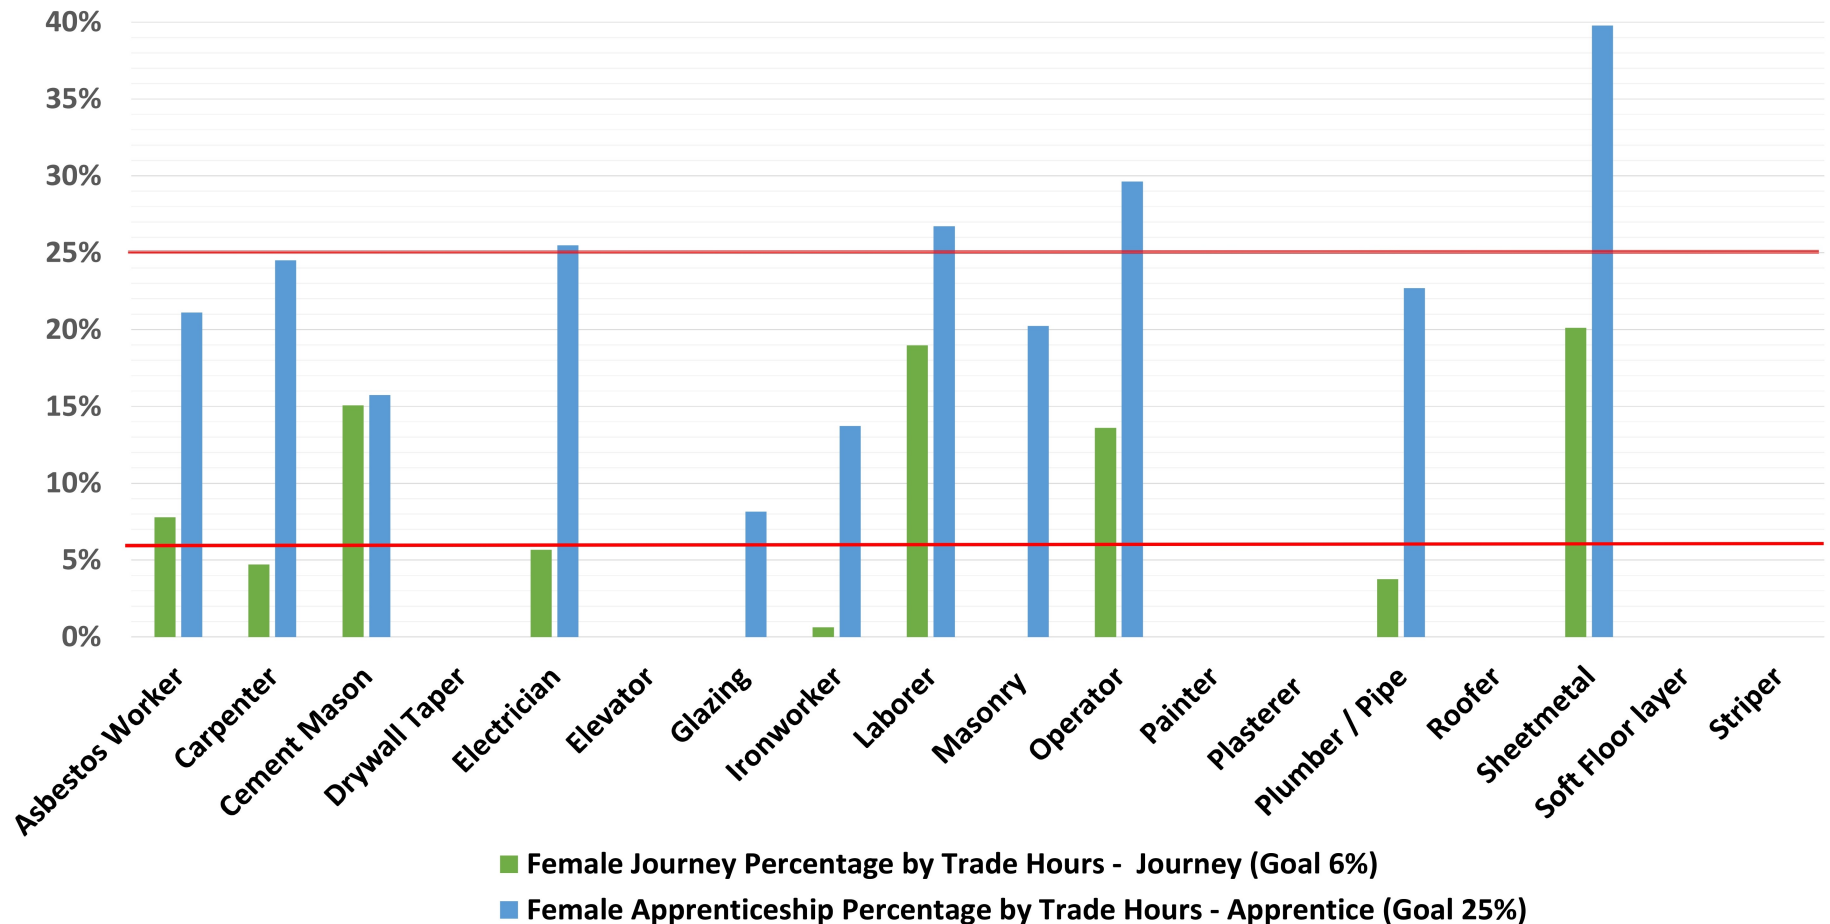

Cumulative Construction Data from 10/31/2016 to 3/31/2019

WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.




March 2019 MCCCH

Construction Workforce Dashboard


Project Summary–


- Exceeding MWSDVESB and overall apprenticeship goal
- 415+ workers daily – diversity continues to increase
- Growing existing MWESB subcontracts by adding scope
- Green Dot training for 28 new field workers
- Project Percent Complete 61%

Total Male Workforce By Ethnicity



Total Female Workforce Ethnicity

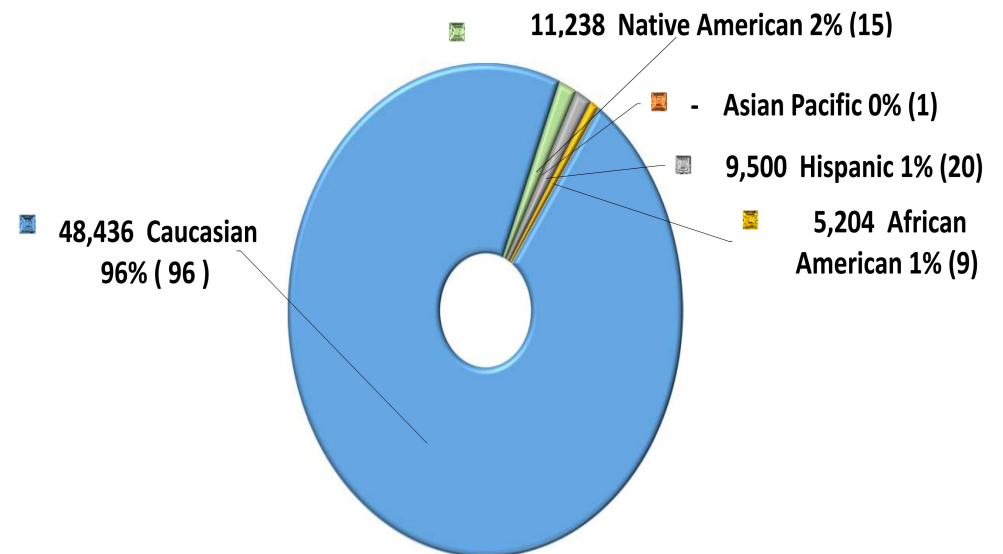




March 2019 MCCCH Construction

MWSDVESB Actual vs Forecast Percentage

Project Percent Complete 61%

MCCCH MWSDVESB Current Percentage 31.8% - March 2019

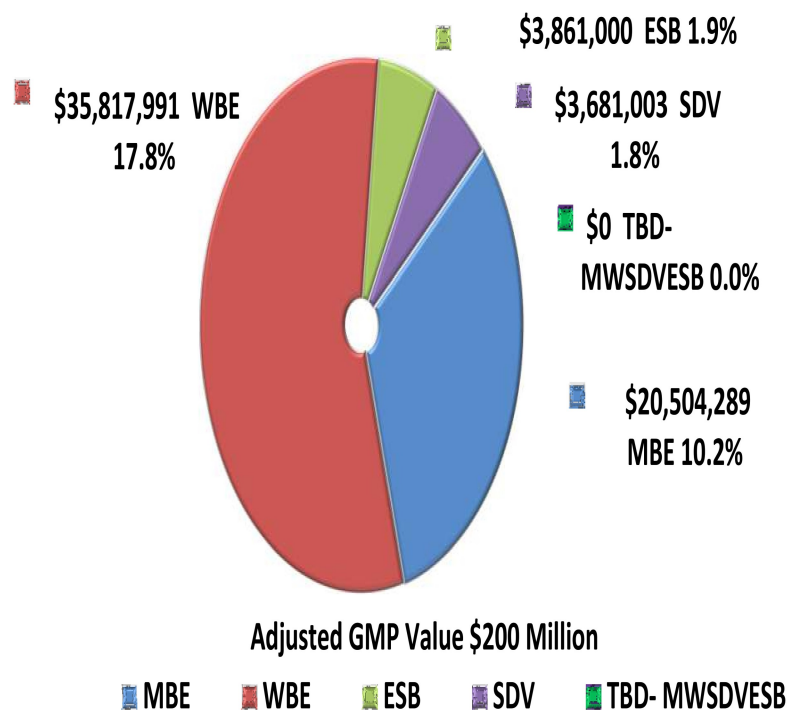

MCCCH MWSDVESB Forecast Percentage 30.1% - Dec 2020

